


Crosstown LRT Project – Update, February 15, 2019

- Crosslinx has confirmed that the scaffolding will remain up until March 31, 2019.
- Minimal work has been completed during the week Feb. 11 due to inclement weather.

WHAT TO EXPECT NEXT WEEK

- Crews will remove a wall below-grade at Brownlow Ave and Eglinton Ave East to complete the installation of the new storm sewer. The work is expected to take approximately 2-3 days to complete. Pedestrians will be routed around the work zone. A flag person will be stationed at the site to provide traffic control.
- Old storm sewer infrastructure will be removed from the southwest work zone.
- These activities, which will take place Monday through Sunday between 7 a.m. and 11 p.m., might generate some noise.

CONSTRUCTION STAGING

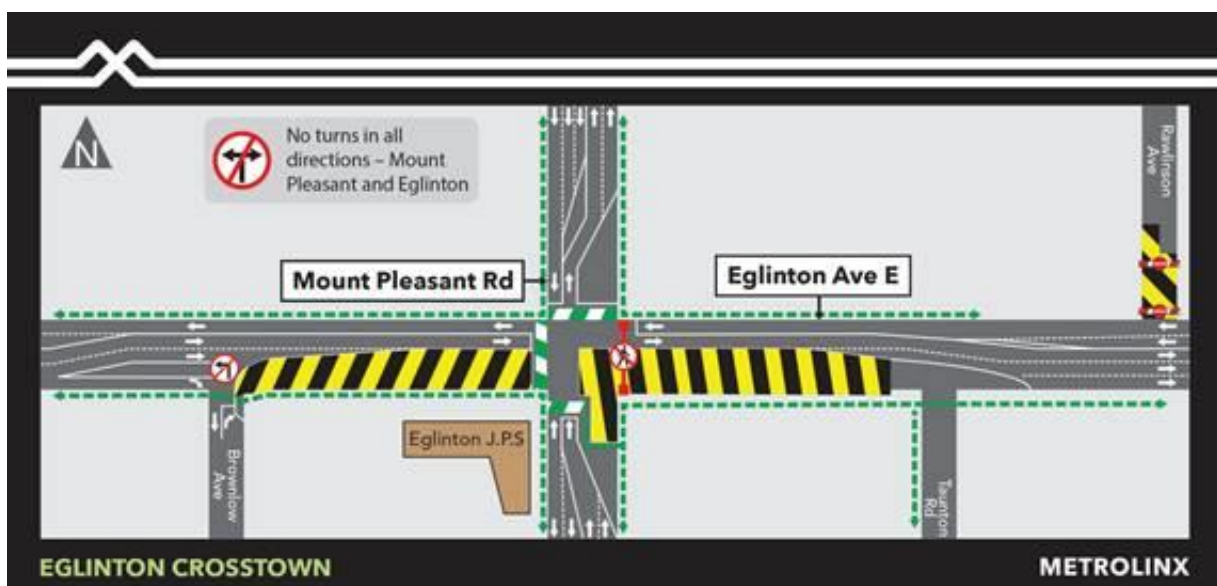

Please visit the [school](#) and [Crosstown LRT](#) websites for regular updates.
