


Wilmington Elementary School Restoration December 8, 2022



Site Plan

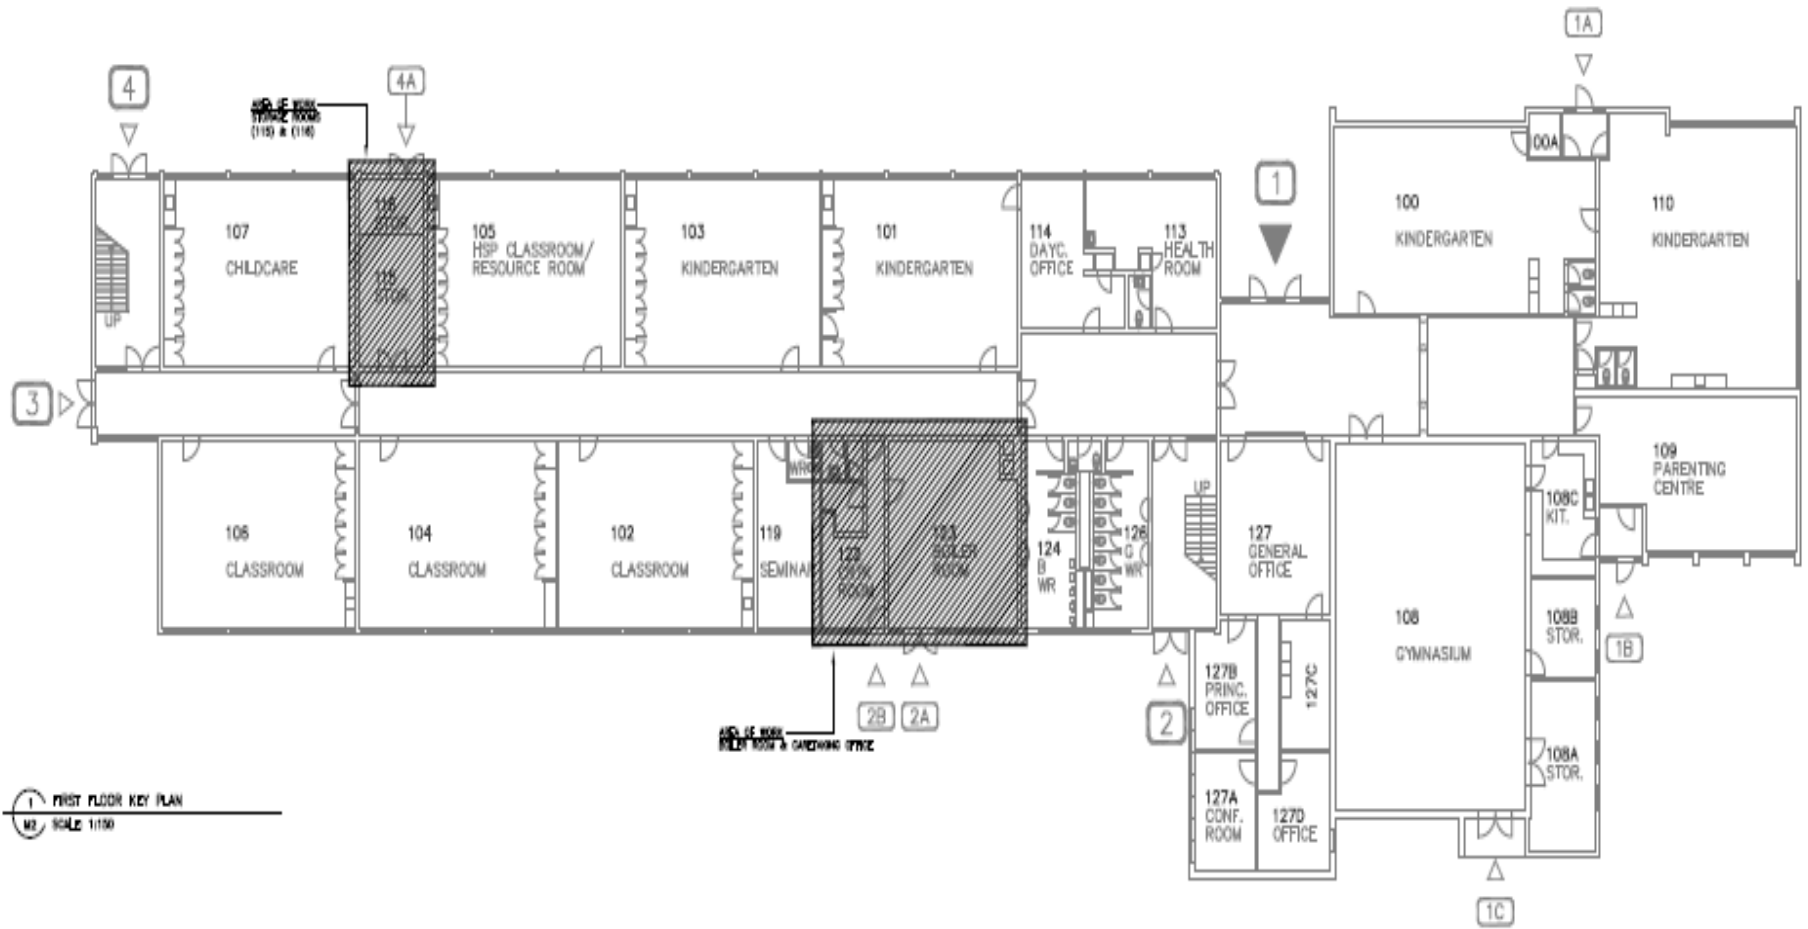

Construction Update

Activity	Location	Approx. Start Date & Duration
Demolition and Abatement	Throughout the first floor	Complete
Heating Plant Installation	Mechanical Room	Underway, one boiler is online, heat turned back on
Gym Floor	Gym	Underway, completion by December 14
Mechanical, Electrical, Fire Protection Rough-In	Throughout the first floor	Underway, approx. one (1) week remaining
Electrical Ductbank	Bus Loop	Complete

Construction Update

Activity	Location	Approx. Start Date & Duration
New Water Supply and Meter, Fire Line	From new meter room to property line by bus loop	To be complete by December 16, 2022
Fire Pump Installation	Meter Room	To be installed by December 23, 2022
Interior Finishing (drywall, flooring, millwork, painting)	First Floor	To be complete by December 30, 2022
Building Inspection for Occupancy	First Floor	January 6, 2023

Wilmington Elementary School – School Restoration – December 8, 2022




Wilmington Elementary School – School Restoration – December 8, 2022



Wilmington Elementary School – School Restoration – December 8, 2022



Wilmington Elementary School – School Restoration – December 8, 2022

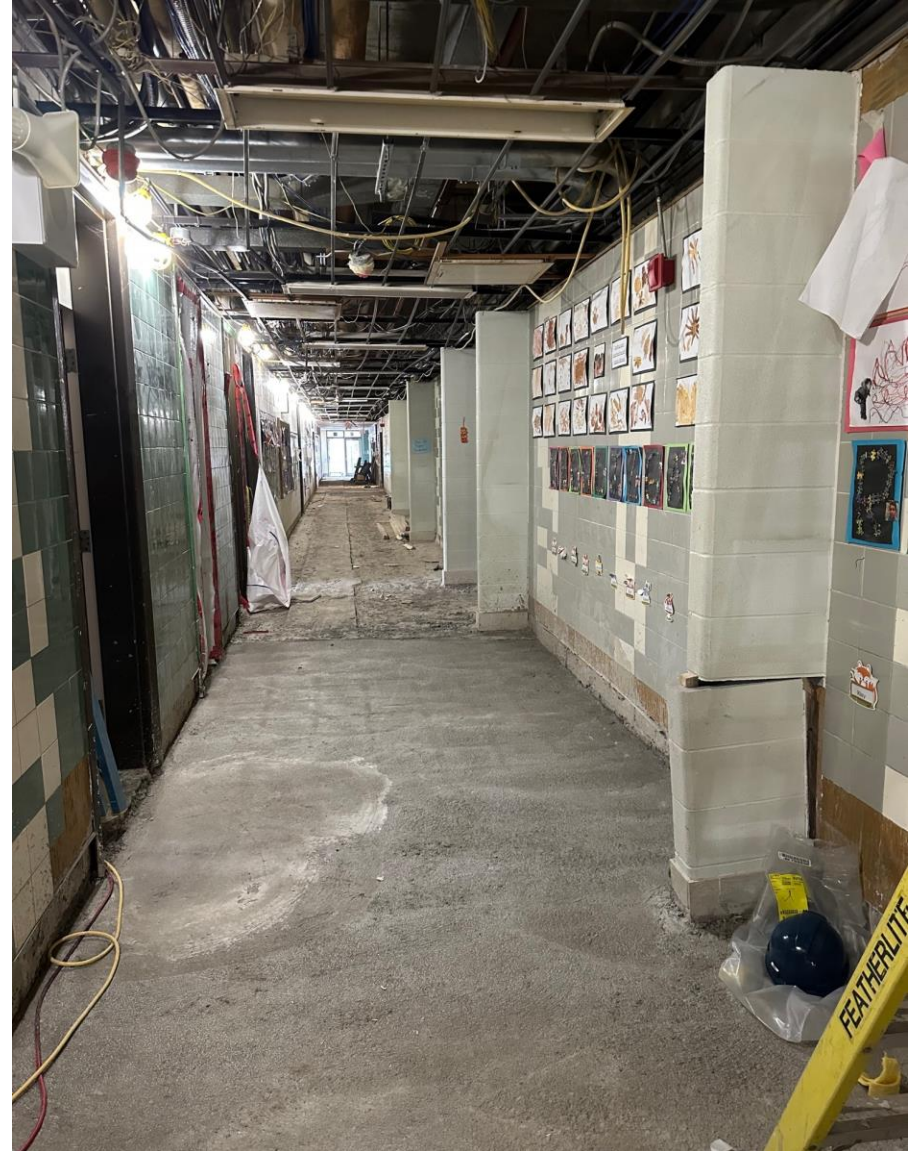

Wilmington Elementary School – School Restoration – December 8, 2022



Wilmington Elementary School – School Restoration – December 8, 2022



