



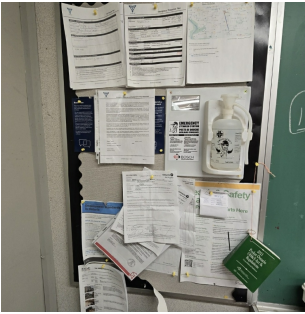




Site Safety Inspection Report



Safety Design Strategies - 410 Chrislea Road, Unit #13, Woodbridge, ON L4L 8B5 - 905-264-7233 - www.sds-safety.com

Company Toronto District School Board	Location/Address 357 Runnymede Road, High Park North, Old Toronto, Ontario, M6P 3C5, Canada		
Date June 23, 2025	Time In: 8:00 AM	Time Out: 10:00 AM	Weather Scattered Clouds, 25°C, 4 km/h Winds
Project	Supervisor TCM - Cillian	Safety Inspector Nicole Stephens	Title TDSB Site Inspection Report for Runnymede JSPS at 357 Runnymede Rd Project Jun 23, 2025

Item #	Act / Reg / Follow-Up	Observations
1. 	Item Site Information INFO Regulation Site Information INFO Action N/A	SDS arrived on site at 8:00 am to observe the construction work being performed at Runnymede JSPS and how the work is effecting the school and its occupants. Discussed site conditions with Paul. Observed ten workers on site and work consists of concrete repairs and roofing.
2. 	Item Bump Lines Regulation #207 (1) (213/91) Action N/A	Observed that adequate barriers are erected in the work area at least 2 meters from the perimeter of the roof, which meets compliance.
3. 	Item Scaffolding - Access Means Regulation #135 (1)(d) (213/91) Action N/A	Observed an adequate means of access/egress to the scaffolding is available, which meets compliance.

Item #	Act / Reg / Follow-Up	Observations
4. 	Item Drinking Water Regulation #28 (1) (213/91) Action N/A	Observed that drinking water is readily available to the workers at the project, which meets compliance.
5. 	Item Safety Board Regulation #25 (i) OHSA Action N/A	Observed that the project safety board was on site and had the required documentation and postings, which meets the requirements of OHSA.
6. 	Item Housekeeping Regulation #35 (1) (213/91) Action On-Going	Observed waste materials and debris being removed to waste disposal containment areas/bins at least daily, which meets compliance.
7. 	Item Guardrail System - Required Regulation #26.3 (1) (213/91) Action N/A	Observed a work area that had an open side that exposed the workers to a fall of greater than 2.4 meters with an adequate guardrail in place, which meets compliance.
8. 	Item Material Storage Regulation #39 (213/91) Action N/A	Observed scaffolding materials on site stored in a manner to prevent tipping, collapsing or rolling as to not endanger a worker, which meets compliance.

Item #	Act / Reg / Follow-Up	Observations
9.	 <p>Item Fencing - Public Way Protection</p> <p>Regulation #65 (213/91)</p> <p>Action Supervisor</p>	Observed fencing installed at least 1.8 meters in height between the project location and the public way, however openings were observed; which endangers the public. Supervisor shall ensure the openings are closed and secure for the protection of public traffic to meet compliance.
10.	 <p>Item Signage</p> <p>Regulation #44 (1) (2) (213/91)</p> <p>Action N/A</p>	Observed that signage containing the word DANGER is posted in prominent areas and in sufficient numbers to warn workers and the public of the hazards on site, which meets compliance.

 <p>TCM - Cillian</p>	 <p>Nicole Stephens</p>
<p>The INSPECTOR believes the information contained within this risk assessment report to be correct at the time of reporting. The INSPECTOR does not accept responsibility for any consequences arising from the use of the information herein. The report is based on matters which were observed or came to the attention of the INSPECTOR during the day of the assessment and should not be relied upon as a final record of all possible risks or hazards that may exist or potential improvements that can be made. It is recommended that all health and safety concerns noted on this report be reviewed and addressed by the client's project Supervisor.</p>	
