


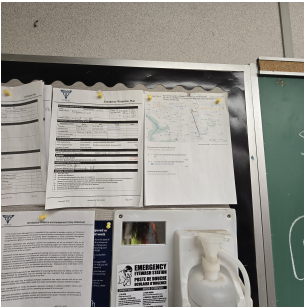








# Site Safety Inspection Report

Safety Design Strategies - 410 Chrislea Road, Unit #13, Woodbridge, ON L4L 8B5 - 905-264-7233 - [www.sds-safety.com](http://www.sds-safety.com)

Company Toronto District School Board	Location/Address 357 Runnymede Road, High Park North, Old Toronto, Toronto, Ontario, M6P 3C5, Canada		
Date June 16, 2025	Time In: 8:00 AM	Time Out: 10:00 AM	Weather Clear Sky, 19°C, 9 km/h Winds
Project	Supervisor TCM - Cillian	Safety Inspector Nicole Stephens	Title TDSB Site Inspection Report for Runnymede JSPS at 357 Runnymede Rd Project Jun 16, 2025

Item #	Act / Reg / Follow-Up	Observations
1. 	<b>Item</b> Site Information INFO <b>Regulation</b> Site Information INFO <b>Action</b> N/A	SDS arrived on site at 8:00 am to observe the construction work being performed at Runnymede JSPS and how the work is effecting the school and its occupants. Discussed site conditions with Paul. Observed ten workers on site and work consists of concrete repairs and roofing.
2. 	<b>Item</b> Ladders for Access / Egress - Securement <b>Regulation</b> #82 (2)(d) (213/91) <b>Action</b> Issue Corrected	Per previous report, observed that a ladder being used as access/egress is now secure at the top and bottom to prevent ladder movement, which meets compliance.
3. 	<b>Item</b> Flammable Liquid Storage <b>Regulation</b> #43 (2) (213/91) <b>Action</b> N/A	Observed that flammable liquids are being stored in well ventilated areas, which meets compliance.

Item #	Act / Reg / Follow-Up	Observations
4. 	<b>Item</b> Constructor - ERP Posting <b>Regulation</b> #17 (3) (213/91) <b>Action</b> N/A	Observed that an emergency response plan was posted on the site and is readily available to the workers, which meets compliance.
5. 	<b>Item</b> Facilities - Location / Service <b>Regulation</b> #29 (7) (9) (11) (213/91) <b>Action</b> N/A	Observed facilities supplied at the project which meets the table in section 29.1 of the regulation. Also observed service records for facilities and location of facilities, which meets compliance.
6. 	<b>Item</b> Fire Extinguisher - Inspection <b>Regulation</b> #55 (213/91) <b>Action</b> N/A	Observed fire extinguisher with inspection tags in place and inspections dated and signed off monthly, which meets compliance.
7. 	<b>Item</b> Overhead Protection - Public Way <b>Regulation</b> #64 (1) (213/91) <b>Action</b> N/A	Observed overhead protection installed for public way protection for a project located 4.5 meters or less from the public way, which meets compliance.
8. 	<b>Item</b> Scaffolding - Footings, Sills, Supports <b>Regulation</b> #128 (1)(c) (213/91) <b>Action</b> N/A	Observed that the footings, sills and supports of the scaffolding are level and secure, which meets compliance.

Item #	Act / Reg / Follow-Up	Observations
9. 	<b>Item</b> Fencing - Public Way Protection <b>Regulation</b> #65 (213/91) <b>Action</b> Issue Corrected	Observed fencing installed at least 1.8 meters in height between the project location and the public way, however openings were observed; which endangers the public. Discussed the issue with the supervisor and the openings were then closed and secure for the protection of public traffic, which meets compliance.
10. 	<b>Item</b> Access / Egress - Work Areas <b>Regulation</b> #70 (1) (213/91) <b>Action</b> N/A	Observed access/egress to and from work areas to be by means of ramp or ladder, which meets compliance.

The INSPECTOR believes the information contained within this risk assessment report to be correct at the time of reporting. The INSPECTOR does not accept responsibility for any consequences arising from the use of the information herein. The report is based on matters which were observed or came to the attention of the INSPECTOR during the day of the assessment and should not be relied upon as a final record of all possible risks or hazards that may exist or potential improvements that can be made. It is recommended that all health and safety concerns noted on this report be reviewed and addressed by the client's project Supervisor.
