












# Site Safety Inspection Report

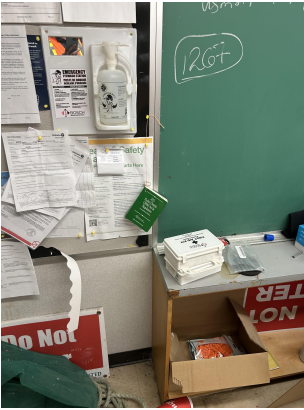

Safety Design Strategies - 410 Chrislea Road, Unit #13, Woodbridge, ON L4L 8B5 - 905-264-7233 - [www.sds-safety.com](http://www.sds-safety.com)

Company Toronto District School Board	Location/Address 357 Runnymede Road, High Park North, Old Toronto, Toronto, Ontario, M6P 3C5, Canada		
Date May 27, 2025	Time In: 8:30 AM	Time Out: 10:30 AM	Weather Few Clouds, 14°C, 3 km/h Winds
Project	Supervisor TCM - Cillian	Safety Inspector Mike Harrison	Title TDSB Site Inspection Report for Runnymede JSPS at 357 Runnymede Rd Project May 27, 2025

Item #	Act / Reg / Follow-Up	Observations
1. 	<b>Item</b> Site Information INFO <b>Regulation</b> Site Information INFO <b>Action</b> N/A	SDS arrived on site at 8:30am to observe the construction work being performed at Runnymede JSPS and how the work is effecting the school and its occupants. Discussed site conditions with Cillian. Observed four workers on site and work consists of chipping.
2. 	<b>Item</b> Scaffolding - Bracing <b>Regulation</b> #128 (1)(a) (213/91) <b>Action</b> N/A	Observed that the uprights of the scaffolding have been braced diagonally in the horizontal and vertical planes to prevent lateral movement, which meets compliance.
3. 	<b>Item</b> Site Information INFO <b>Regulation</b> Site Information INFO <b>Action</b> N/A	Observed postings in prominent areas informing the workers of the required PPE on site.
4. 	<b>Item</b> Material Storage <b>Regulation</b> #39 (213/91) <b>Action</b> N/A	Observed wood and other materials on site stored in a manner to prevent tipping, collapsing or rolling as to not endanger a worker, which meets compliance.

Item #	Act / Reg / Follow-Up	Observations
5. 	<b>Item</b> First Aid Station <b>Regulation</b> #1 (1) (1101) <b>Action</b> N/A	Observed that a first aid station had an adequately supplied first aid kit for their workforce, Form 82 posted, and the certificates of trained first aiders on duty, which meets compliance.
6. 	<b>Item</b> Scaffolding - Unguarded Openings <b>Regulation</b> #135 (1)(e) (213/91) <b>Action</b> N/A	Observed that openings in the scaffolding are guarded by a hatch and closed to ensure the safety of the worker, which meets compliance.
7. 	<b>Item</b> Flammable Liquid Storage <b>Regulation</b> #43 (2) (213/91) <b>Action</b> N/A	Observed that flammable liquids are being stored in well ventilated areas, which meets compliance.
8. 	<b>Item</b> Fencing - Public Way Protection <b>Regulation</b> #65 (213/91) <b>Action</b> N/A	Observed fencing installed at least 1.8 meters in height between the project location and the public way for the protection of public traffic, which meets compliance.
9. 	<b>Item</b> Constructor - ERP Posting <b>Regulation</b> #17 (3) (213/91) <b>Action</b> Issue Corrected	Observed that an emergency response plan was posted on the site and is readily available to the workers, which meets compliance.

Item #	Act / Reg / Follow-Up	Observations
10.	 <p><b>Item</b> Lighting <b>Regulation</b> #45 (1) (213/91) <b>Action</b> N/A</p>	Observed lighting was available for the areas of work to provide adequate lighting for the workers, which meets compliance.
11.	 <p><b>Item</b> Dust Control <b>Regulation</b> #59 (213/91) <b>Action</b> N/A</p>	Observed the work area is sealed to prevent dust from getting into open areas around the work area, which meets compliance.

 <p>TCM - Cillian</p>	 <p>Mike Harrison</p>
--	--

The INSPECTOR believes the information contained within this risk assessment report to be correct at the time of reporting. The INSPECTOR does not accept responsibility for any consequences arising from the use of the information herein. The report is based on matters which were observed or came to the attention of the INSPECTOR during the day of the assessment and should not be relied upon as a final record of all possible risks or hazards that may exist or potential improvements that can be made. It is recommended that all health and safety concerns noted on this report be reviewed and addressed by the client's project Supervisor.
